CT PERFORMANCE EVALUATION REPORT

PRE-TEST / POST FAN CHANGE / POST DISTRIBUTION CHANGE

— THREE-STAGE SINGLE CELL ASSESSMENT —

COOLING TOWER — CELL 2 | 3-FAN INDUCED DRAFT

OWNER / CLIENT	DUMMY INDUSTRIES LTD.
TESTING AGENCY	SS COOLING TOWER CONSULTANTS (SSCTC)
DATE OF TEST	12-Mar-2026
REPORT DATE	19-Apr-2026
ASSESSMENT METHOD	CTI ATC-105 Merkel Method — Applied independently to each of 3 test stages

CONFIDENTIAL — This report is prepared exclusively for the above-named client by SS Cooling Tower Consultants. It may not be reproduced, distributed, or disclosed to any third party without prior written consent of SSCTC.

PREAMBLE

This report presents the CT performance evaluation for Cell 2.

MEMBERS PRESENT FOR THE TEST

CLIENT

- Mr. A. Sharma — Plant Manager

SS COOLING TOWER CONSULTANTS (SSCTC)

- Er. R. Mehta — Lead Test Engineer

ASSESSMENT METHOD & ANALYSIS

The CTI ATC-105 Merkel method is applied independently.

INSTRUMENT PLACEMENT AND READINGS

Wet Bulb: aspirated psychrometer at inlet.

CONCLUSION AND REMARKS

1. Cell 2 was below design by 1.85 degC.

SUGGESTIONS AND SPECIAL NOTES

1. Re-verify fan pitch every 6 months.

FINAL DATA AND CONCLUSION OF PRE AND POST TEST

The following table presents a consolidated comparison of all measured and calculated parameters across the three test stages conducted during this evaluation.

Parameter	Unit	TEST 1 Pre-Test	TEST 2 Post Fan Change	TEST 3 Post Distr.
Water Flow Rate	m3/hr	850	853	856

NOTES

1. All temps in Celsius.

ATC-105 PERFORMANCE EVALUATION — TEST 1 — PRE TEST

DESIGN VS RECORDED TEST CONDITIONS

Parameter	Unit	Design Conditions	Recorded Test Conditions
Water Flow	m³/hr	900.00	850.00
Hot Water Temp	°C	40.00	42.10
Cold Water Temp	°C	28.00	29.85
Wet Bulb Temp	°C	24.00	24.50
Range	°C	12.00	12.25
Approach	°C	4.00	5.35

STEP 1

TABLE 1 — CWT vs Range at Test WBT

Using the Merkel method, predicted Cold Water Temperatures (CWT) are computed at three fan speeds (90%, 100%, 110% of design flow) for three range values (80%, 100%, 120% of design range) at the recorded Test Wet Bulb Temperature.

Range %	Range (°C)	CWT @ 90% Flow	CWT @ 100% Flow	CWT @ 110% Flow
80%	9.6 °C	26.80	25.60	24.60
100%	12.0 °C	28.90	27.70	26.50
120%	14.4 °C	30.80	29.50	28.30

STEP 2 — CROSS PLOT 1 — CWT vs Range at Test WBT

Plot the three CWT lines (90%, 100%, 110% flow) from Table 1 against Range. Draw a vertical line at the Test Range to read off the CWT for each flow condition. These three (Flow, CWT) pairs form Table 2.

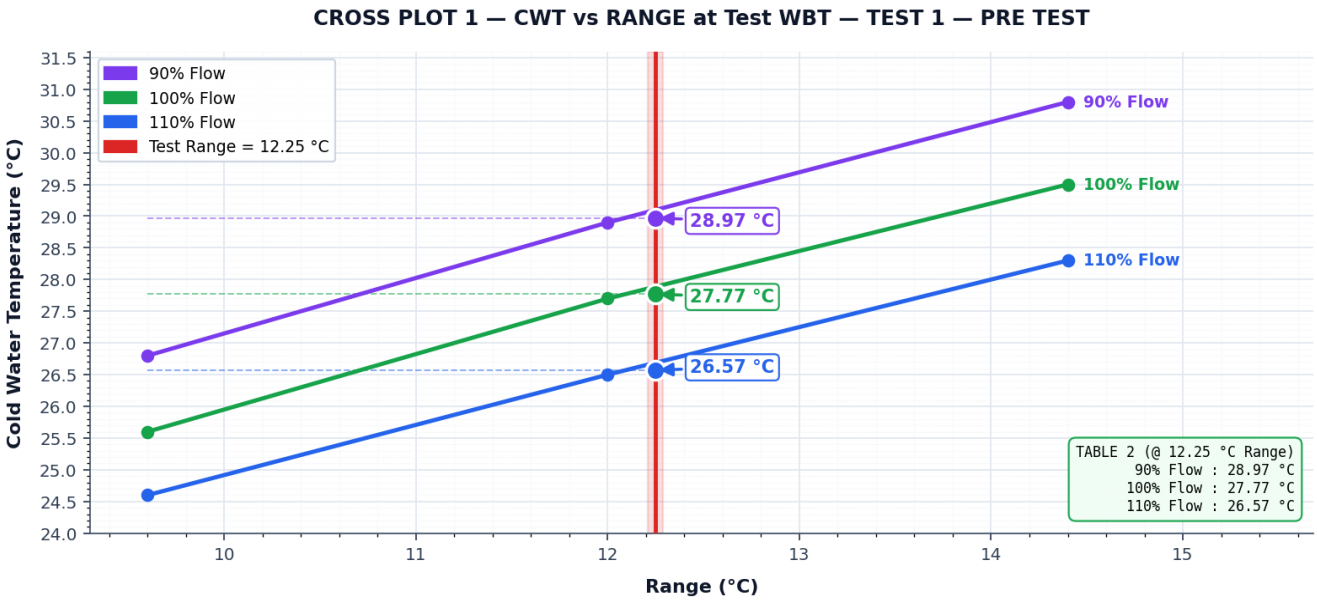

Figure 1: Cross Plot 1 — CWT vs Range at Test WBT — TEST 1 — PRE TEST

TABLE 2 — CWT at Test Range = 12.25 °C

Flow Condition	Water Flow (m³/hr)	CWT at Range 12.25°C
90% Flow	810.00	28.97
100% Flow	900.00	27.77
110% Flow	990.00	26.57

STEP 3 ADJUSTED WATER FLOW — Air Density Correction

Adjust the recorded water flow for air density differences between test and design conditions: Q_adj = Q_test × (Air Density Ratio)^0.5. The density ratio accounts for atmospheric variation in air mass flow delivered by the fan.

i. Recorded Test Water Flow (Q_test)	**850.00 m³/hr**
ii. Air Density Ratio (ρ_design / ρ_test)	**1.00**
iii. CWT @ 90% Design Flow (Cross Plot 1)	**28.97 °C**
iv. CWT @ 100% Design Flow (Cross Plot 1)	**27.77 °C**
v. CWT @ 110% Design Flow (Cross Plot 1)	**26.57 °C**
vi. Test Hot Water Temperature (HWT)	**42.10 °C**
vii. Test Cold Water Temperature (CWT)	**29.85 °C**
viii. Test Wet Bulb Temperature (WBT)	**24.50 °C**
Q_adj — Adjusted Water Flow (Density Corrected)	**847.20 m³/hr**

STEP 4 CROSS PLOT 2 — Water Flow vs CWT (Design WBT & Range)

Plot (Water Flow, CWT) pairs from Table 2. Locate Q_adj on the performance curve to read the Predicted CWT. Then find the water flow where the curve meets the Design CWT — this is the Predicted Flow used in Step 5.

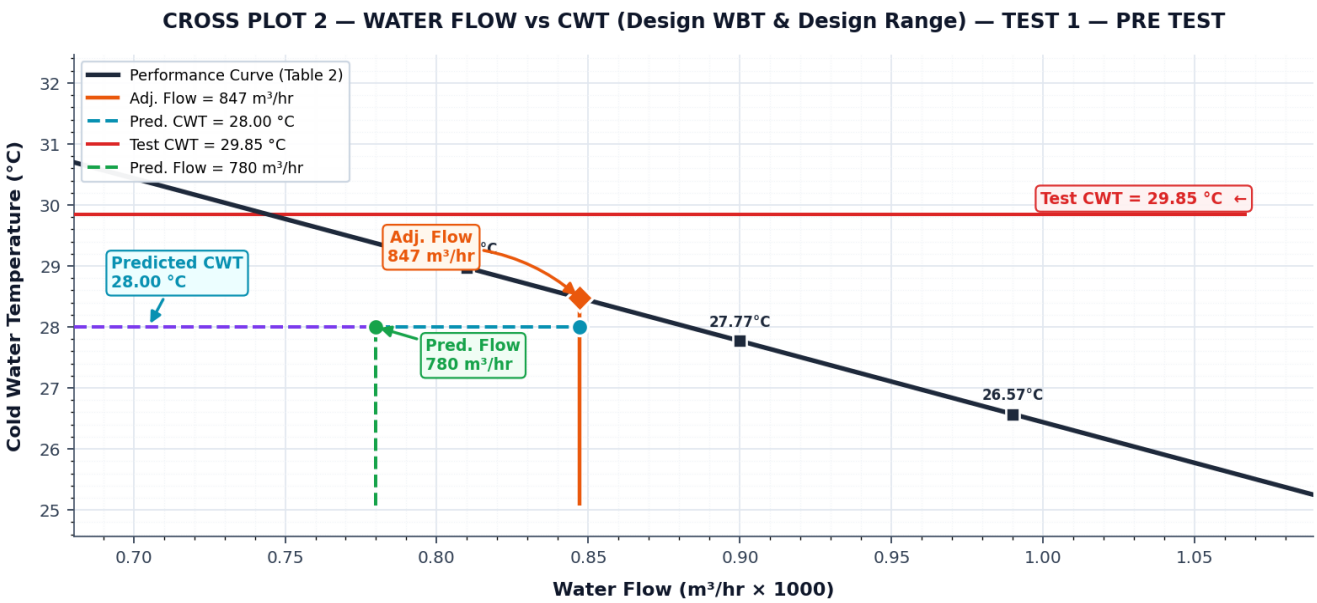

Figure 2: Cross Plot 2 — Water Flow vs CWT (Design WBT & Range) — TEST 1 — PRE TEST

FINAL ATC-105 RESULTS — TEST 1 — PRE TEST

STEP 5 FINAL EVALUATION — CWT Shortfall & Capability

Compare the Predicted CWT (from Cross Plot 2 at Q_adj) with the Test CWT. CWT Shortfall = Test CWT – Predicted CWT. A negative shortfall means the tower performed below specification. Capability % = (Q_adj / Predicted Flow) × 100.

Step	Parameter	Value
i	Q_adj — Adjusted Water Flow (density corrected)	847.20 m³/hr
ii	Predicted CWT — from Cross Plot 2 at Q_adj	28.00 °C
iii	Test CWT — Recorded during test	29.85 °C
iv	Predicted Water Flow — at Design CWT on Cross Plot 2	780.00 m³/hr
v	CWT Shortfall = Test CWT – Predicted CWT	-1.85 °C
vi	Cooling Tower Capability = (Q_adj / Pred. Flow) × 100	108.60 %
vii	Air Density Ratio applied	1.00

CONCLUSION — TEST 1 — PRE TEST

CWT SHORTFALL IN PERFORMANCE

-1.85 °C

Test CWT (29.85°C) vs Predicted CWT (28.00°C)

COOLING TOWER CAPABILITY

108.6 %

= 847 / 780 × 100

Tower is **BELOW specification** by 1.85°C — Capability: **108.6%**

——— END OF REPORT ———

SS COOLING TOWER CONSULTANTS
www.ssctc.org
19-Apr-2026
